



**BEFORE THE PUBLIC UTILITIES COMMISSION OF THE  
STATE OF CALIFORNIA**

**FILED**  
5-27-14  
04:59 PM

In the Matter of the Application of SOUTHERN )  
CALIFORNIA EDISON COMPANY (U 338-E) ) Application 07-06-031  
for a Certificate of Public Convenience and ) (Filed June 29, 2007)  
Necessity Concerning the Tehachapi Renewable )  
Transmission Project (Segments 4 through 11) )  
\_\_\_\_\_ )

**SOUTHERN CALIFORNIA EDISON COMPANY'S (U 338-E)**  
**NOTICE OF *EX PARTE* COMMUNICATION**

**PUBLIC VERSION**

BETH GAYLORD  
ANGELA WHATLEY

Attorneys for  
SOUTHERN CALIFORNIA EDISON COMPANY

2244 Walnut Grove Avenue  
Post Office Box 800  
Rosemead, California 91770  
Telephone: (626) 302-3618  
Facsimile: (626) 302-1926  
E-mail: [angela.whatley@sce.com](mailto:angela.whatley@sce.com)

Dated: May 27, 2014

**BEFORE THE PUBLIC UTILITIES COMMISSION OF THE  
STATE OF CALIFORNIA**

In the Matter of the Application of SOUTHERN )	
CALIFORNIA EDISON COMPANY (U 338-E) )	Application 07-06-031
for a Certificate of Public Convenience and )	(Filed June 29, 2007)
Necessity Concerning the Tehachapi Renewable )	
Transmission Project (Segments 4 through 11) )	
_____ )	

**SOUTHERN CALIFORNIA EDISON COMPANY'S (U 338-E)  
NOTICE OF EX PARTE COMMUNICATION**

Pursuant to Rule 8.4 of the California Public Utilities Commission (Commission) Rules of Practice and Procedure, Southern California Edison Company (SCE) hereby gives notice of the *ex parte* communication described below.

At approximately 2:00 p.m., on May 21, 2014, Kevin Cini, Vice President, Major Projects; Douglas Bauder, Vice President Supply Management, Operational Service; Robert Boada, Vice President and Treasurer; George Tabata, Assistant Treasurer, Financing, Banking & Credit; Thomas Burhenn, Director, Regulatory Licensing; Marc Chazaud, Principle Manager, Credit, Risk & Collateral; Daniel Jackson, Project Manager, Credit, Risk & Collateral; Susan J. Nelson, Principle Advisor, Infrastructure Licensing, and Sandra Blain, Principle Manager, Major Construction Projects met with Audrey Lee, Energy Advisor to President Peevey; Edward Randolph, Director, Energy Division; Molly Sterkel, Manager, Infrastructure Planning & Permitting Branch; Mary Jo Boark, Supervisor, Infrastructure Planning & Permitting Branch, and Jason Coontz, Project Manager, Infrastructure Planning & Permitting Branch. The meeting was telephonic. The Commission requested the meeting, which lasted approximately 60

minutes. SCE representatives discussed the status of the TRTP Project relative to undergrounding in Chino Hills.

A PowerPoint presentation was used in the discussion and distributed to Commission attendees. Because the presentation contains confidential information, a public, redacted version is being filed, along with a confidential version pursuant to California Public Utilities Code, section 583 and General Order 66(c), discussed in more detail in SCE's concurrently-filed Motion to File Under Seal. The redacted PowerPoint is provided in Attachment A.

Dated: May 27, 2014

Respectfully submitted,

/s/ Angela Whatley

By: Angela Whatley

Attorney for  
SOUTHERN CALIFORNIA EDISON COMPANY

2244 Walnut Grove Avenue  
Post Office Box 800  
Rosemead, CA 91770  
Telephone: (626) 302-3618  
Facsimile: (626) 302-1926  
E-mail: [angela.whatley@sce.com](mailto:angela.whatley@sce.com)

**ATTACHMENT A**

# Tehachapi Renewable Transmission Project Update

California Public Utilities Commission

May 21, 2014


**REDACTED VERSION**

# Agenda

Provide status on:

- Civil Purchase Order
- Eastern Transition Station (ETS) Environmental Status
- Real Properties
- Environmental Permits
- Cable Suppliers
- Public Agencies
- Safety
- Back-Up
  - Changes in Schedule
  - Schedule

# Civil Award



- Civil award is anticipated in the next 2 weeks, but start of construction may be delayed pending resolution on
  - Final land rights
  - Receipt of environmental permits
  - Finalization of Eastern Transition Station (ETS) contamination with San Bernardino County and Regional Water Quality Control Board (RWQCB)


# Eastern Transition Station (ETS)

- San Bernardino County Memorandum Of Understanding (MOU) on Contamination
  - MOU was sent to the County of San Bernardino. It has SCE as the lead and proposes SCE to accept cost responsibility, County of San Bernardino is still a Responsible Party (RP)
    - Summary of Cost:
      - Best case - \$750,000 (Capital Costs - \$635,000; O&M Costs - \$115,000 for 4 years)
      - Most likely case - \$1,500,000 (Capital Costs - \$1,172,500; O&M Costs - \$327,500 for 6 years)
      - Worst case - \$3,500,000 (Capital Costs - \$2,590,000; O&M Costs - \$910,000 for 9 years)
  - No major changes expected following County review
  - Board of Supervisor approval is needed
- May 2, the team had a phone discussion with Regional Water Quality Control Board (RWQCB) and San Bernardino County Certified Unified Program Agency on process
- May 15, SCE submitted formal application to Regional Water Quality Control Board. RWQCB reviewed the SCE Request for Agency Oversight of a Brownfield Site application and agreed to retain oversight of the environmental investigation and remediation activities
- June 3, SCE to meet with San Bernardino County and Regional Water Quality Control Board to discuss the proposed remediation plan and obtain approval

# Real Properties

- There are a total of 57 Acquisitions
  - Consisting of 90 parcels
- After reasonable negotiations, 44 Eminent Domain Actions were filed in San Bernardino Superior Court. Since filing, SCE has been able to reach agreement with the majority of property owners
- Pre-Possession hearings begin June 6. Property Owner Objections needed to be filed by May 15
- By the deadline of May 15, Objections were received
  - Karen Goodwin, a member of Hope for the Hills
    - Opposed possession and claims she is entitled to relocation and construction will be too impactful for anyone to live in the home. She claims the reduction in the size of her backyard eliminates any use of the property and it should be a full take
  - Promenade
    - Opposed after the 30 day opposition period. He did not give reasons for the late opposition, and claims that SCE did not give him an extension to answer. He also claims he has a higher public use than TRTP and is opposing on those grounds
  - Darmal-Kamari
    - Claims SCE has no right to condemn entire property. He claims that he can develop 16 homes on the site. The basis of his claim is that SCE's appraisal values are based as open space and not residential lots. The property is currently zoned as open space
- Two friendly Eminent Domain actions are in process
  - Flood Control (friendly – 2 locations)
  - ETS location (friendly - County and City of CH)

# Real Estate Readiness Map (as of 5/14/2014)

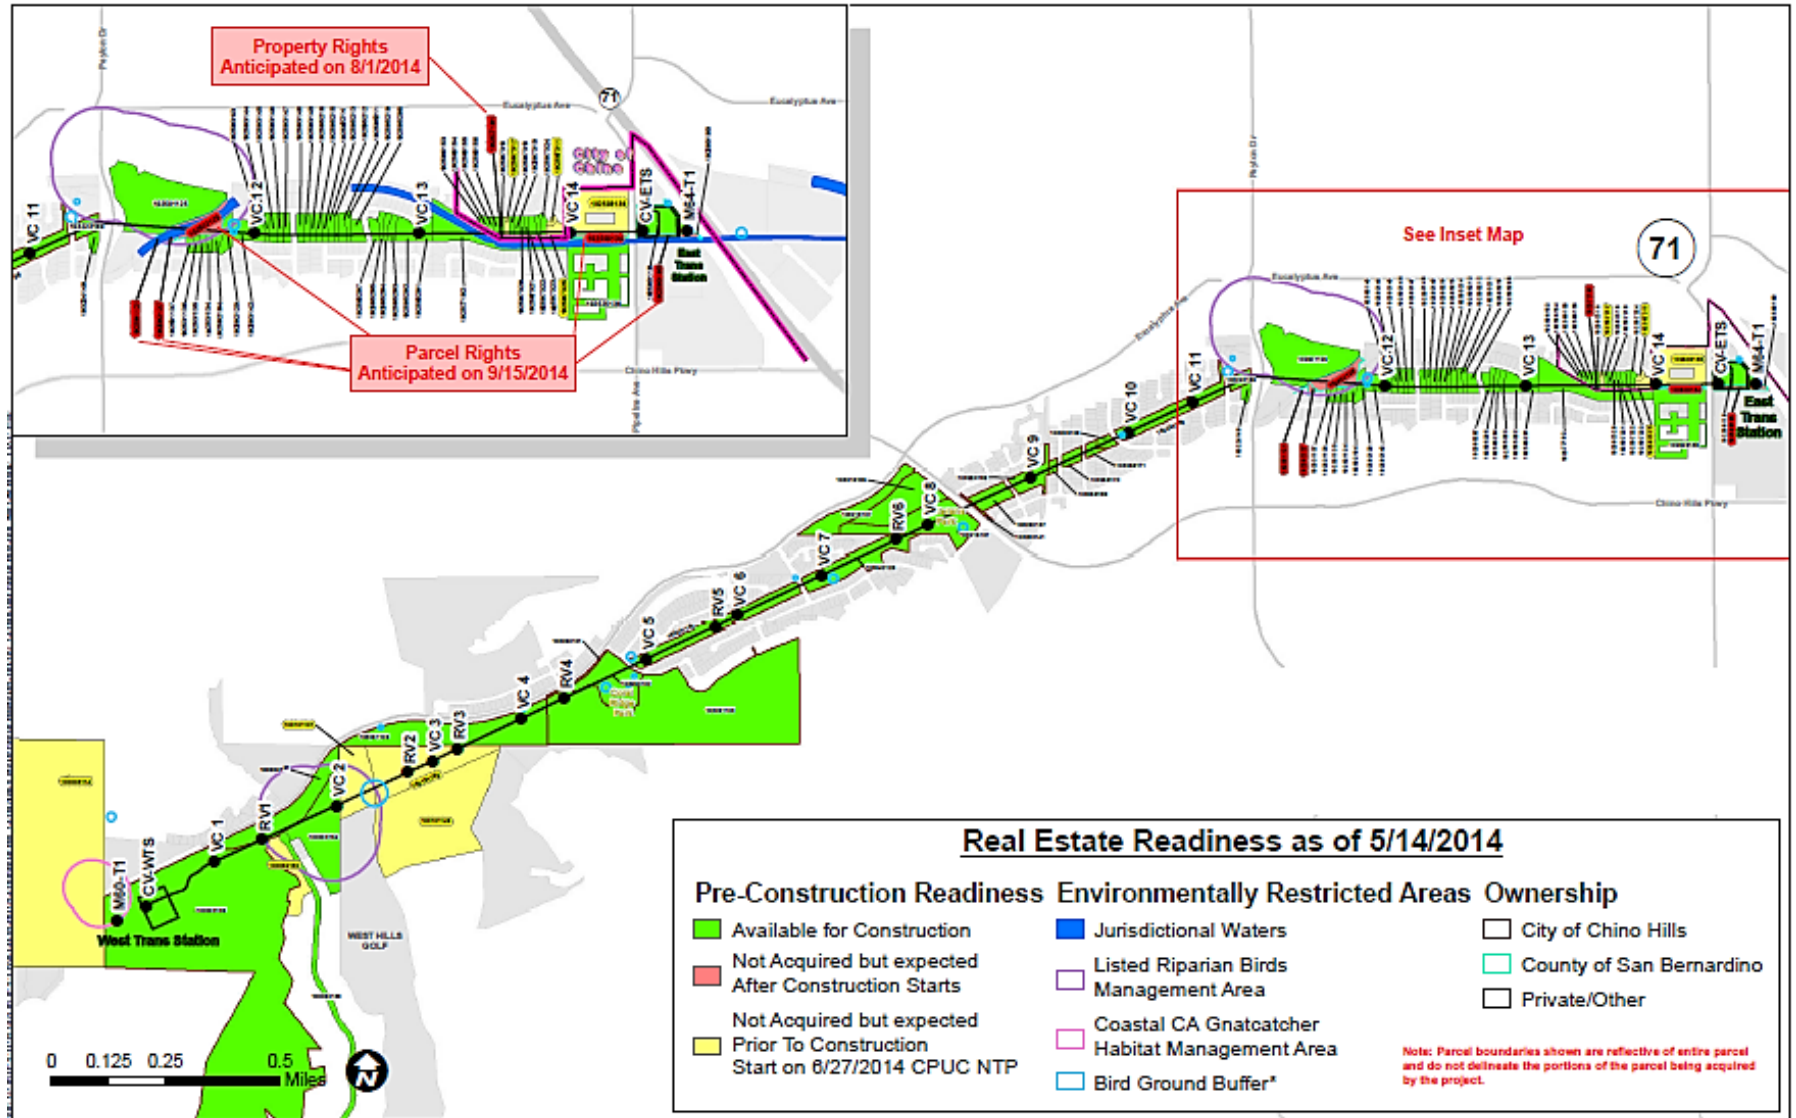

# Permits


## Environmental Permit Status

- Biological Opinion amendment - U.S. Fish and Wildlife Service (USFWS)
  - Permit amendment request submitted: 2/21/14
  - Reconsultation request submitted 4/4/14
  - Permit anticipated: 7/31/14 – SCE team working with CDFW to pull the date back to June 2014
- ITP amendment-California Department of Fish and Wildlife (CDFW)
  - Permit amendment request submitted: 2/7/14
  - Resubmittal to account for CDFW comments: 4/18/14
  - Permit anticipated: 7/31/14
- CDFW 1602, SWRCB 401, and ACOE 404
  - Permit amendment request submitted: 10/15/13
  - Resubmittal to account for engineering changes: 2/15/14
  - Permit anticipated: 1602 – 5/30/14, 401 – 5/30/14, 404 – 6/6/14
  - An additional 45 days is needed for mitigation compliance
- SCE is working with each Agency to expedite receipt of the permits to support construction




# Cable Suppliers

- At the last TRTP Update, April 7, we discussed
  - SCE evaluations in process with six suppliers
    - Five base bid responses and eight alternates
  - SCE worked with each supplier through several design concerns
    - Termination material
    - Corrugated aluminum vs. laminated copper sheath
    - Material and thickness of laminate
    - Temperature (DTS) sensing




# Eliminated Suppliers





Confidential Pursuant to Public Utilities  
Code Section 583

## Cable Suppliers - continued



# Credit Metrics – Remaining Suppliers

(As of 12/31/13)



Confidential Pursuant to Public Utilities  
Code Section 583

# Public/Agency Issues

## Duarte

- Since completion of the soldier pile walls required in the design by the City of Duarte, the City has now demanded a similar finish on other retaining wall(s) due to glare
- SCE is researching the possibility of applying a finish to the other walls, and will make a determination after completion of the road and structures

## La Habra

- Resident concern about TRTP FAA light shining in their home
  - Approximately 1,900 feet distance between the residence and TRTP tower. SCE to visit resident and discuss concern



## Public/Agency Issues

### Mr. & Mrs. Bartoli in the City of Duarte

- Sent letter on May 15 requesting compensation for TRTP impacts

### Chino Hills

- On May 16 received Cease and Desist letter from Oak Tree Downs Property Owners' Association, Inc. The Association will not oppose the project and will allow SCE to use the Association's streets for a fee. SCE holds all necessary rights and will respond formally.


# Safety

## Segments 7 & 8

- On May 8, after a significant number of safety and environmental incidents in a short period of time, SCE issued a Safety and Environmental Stand-Down to PAR
- Incidents preceding the Stand-Down
  - March 19, PAR bent an arm on a 220kV structure during stringing operations
  - April 18, a Notice of Non-Compliance was issued to PAR for failure to properly barricade work zones from the public
  - April 26 and 27, PAR had 9 Level 2 nest buffer incursions by helicopter within a 48-hour period
  - May 6, a Notice of Non-Compliance was issued to PAR for failure to report a hatch falling from a helicopter on April 17
- 5/8/14 – SCE issued Stop Work Notice to PAR after PAR crews lost control of the ground line being pulled near Rose Hills
  - 5/9/14 – SCE held conference call with PAR management team elaborating on the Stop Work Notice and requirement to return to work
  - 5/12/14 – SCE and PAR management meeting held to address Safety
  - 5/13/14 – SCE and PAR management meeting held to address Environmental compliance
    - PAR presented their Recovery Plan
  - 5/14/14 – SCE attended PAR's half day Craft Stand Down meeting
    - SCE released PAR to work
  - 5/20/14 – Follow-up meeting with PAR scheduled
    - New topics from Craft Stand Down meeting
    - 30-day Post Recovery Plan report out

# Back-Up

# Changes in Schedule



# Tentative Schedule & Assumptions – Underground



# Tentative Schedule & Assumptions – Underground



# Reference Schedules

Dated April 1, 2014

Presented April 7, 2014

# Tentative Schedule & Assumptions – Underground



# Tentative Schedule & Assumptions – Underground

